



Friday, June 28, 2019



WHITNEY HILL WIND FARM

24 WTG's
21 GE 2.8 MW & 3 GE 2.3 MW
65 MW Capacity



Substantial Completion

Friday, November 15, 2019

COD

Monday, December 23, 2019

TODAY'S WEATHER FORECAST

Conditions	Sunny	Wind Direction	N	Wind Speed	3 mph	Dew Point	72%	Temperature	High 89	Low 69	Humidity	74%	Precipitation	0%
------------	-------	----------------	---	------------	-------	-----------	-----	-------------	---------	--------	----------	-----	---------------	----

SAFETY						ENVIRONMENTAL					
- review emergency exit plan to transport medical incidents						- n/a					
- All Hands scheduled for July 8; review of procedures after holiday break						-					
- additional speed limit signs installed						-					
DAILY HIGHLIGHTS						PUBLIC ROADS CLOSURES					
- culverts RCP - S52 plate steel & form-up						- (06/28): 200 (1400 to 1325), 400 (2000 to 1842, closed thru 7/8/19), 1500 (200 to 275), 275 (1325 to 1400)					
- culverts CMP/HDPE 25						- (06/29): 1750 (400 to 300), 200 (1400 to 1500), 300 (1750 to T15), 400 (2000 to 1842, closed thru 7/8/19)					
- proof roll completed ; close to optimum moisture levels						- rock and sand delivery @ 1600th and 300th; continued tree removal T11; specialty signage pending					

WORK PROGRESS (AS OF COB LAST WORKING DAY)

ACTIVITY	UNIT	TOTAL QUANTITIES		COMPLETED ACTUAL QTY	REMAINING QUANTITY	WEIGHT (%)	COMPLETED ACTUAL WEIGHTED (%)	COMPLETED LAST WORKDAY		LOCATIONS TO COMPLETE	
		PLANNED	CONFIRMED					LOCATIONS	ACTUAL QTY	TODAY	NEXT WORKDAY
Access Roads Overall Completion											
				0 LF	37,418 LF	100%	0%				
Road Cut	CY	5,816	5,816	0	5816	20%	0%		0		
Road Fill	CY	1,973	1,973	0	1973	20%	0%		0		
Cement Stabilization	CY	15,976	15,976	0	15976	30%	0%		0		
Road Capping	CY	6,091	6,091	0	6091	30%	0%		0		
CREWS: 0 HEADCOUNT: 0											
Public Roads Overall Completion											
				0 LF	63,191 LF	100%	0%				
Cement Stabilization	CY	43,998	43,998	0	43998	30%	0%		0		
Road Capping	CY	15,780	15,780	0	15780	30%	0%		0		
Bituminous Surface Treatment	SQY	131,951	131,951	0	131951	40%	0%		0		
CREWS: 0 HEADCOUNT: 0											
Foundations Overall Completion											
				0 Found.	24 Found.	100%	0%				
Pad Clearing (location)	ea.	24	24	0	24	5%	0%		0		
Excavation	ea.	24	24	0	24	10%	0%		0		
Soil grouting / Subgrade compaction	ea.	24	24	0	24	10%	0%		0		
Mud Mat (Lean concrete)	ea.	24	24	0	24	5%	0%		0		
Foundation Rebar	ea.	24	24	0	24	15%	0%		0		
Bolt cage	ea.	24	24	0	24	10%	0%		0		
Grounding installation	ea.	24	24	0	24	5%	0%		0		
Base section pour	ea.	24	24	0	24	10%	0%		0		
Pedestal section pour	ea.	24	24	0	24	5%	0%		0		
Foundations Backfilled	ea.	24	24	0	24	10%	0%		0		
Ground Resistivity Testing	ea.	24	24	0	24	5%	0%		0		
Crane Pad	ea.	24	24	0	24	10%	0%		0		
CREWS: 0 HEADCOUNT: 0											
Substation Overall Completion											
				97% Remain	100%	3%					
General	%	100%	100%	15%	85%	20.0%	15%		0.0%		
Control / GIS Building	%	100%	100%	0%	100%	7.5%	0%		0.0%		
SCADA Building	%	100%	100%	0%	100%	7.5%	0%		0.0%		
Foundations	%	100%	100%	0%	100%	20.0%	0%		0.0%		
EM Works: High Voltage (HV)	%	100%	100%	0%	100%	15.0%	0%		0.0%		
EM Works: Medium/Low Voltage (MV/LV)	%	100%	100%	0%	100%	15.0%	0%		0.0%		
Pre-Commissioning: General	%	100%	100%	0%	100%	5.0%	0%		0.0%		
Pre-Commissioning: High Voltage (HV)	%	100%	100%	0%	100%	5.0%	0%		0.0%		
Pre-Commissioning: Medium/Low Voltage (MV/LV)	%	100%	100%	0%	100%	5.0%	0%		0.0%		
CREWS: 0 HEADCOUNT: 0											
O&M Building Overall Completion (if applicable)											
				100% Remain	100%	0%					
O&M Building	%	100%	100%	0%	100%	100%	0%		0		
CREWS: 0 HEADCOUNT: 0											
Collection System Overall Completion											
				0 LF	600 LF	100%	0%				
Row clearing	LF	3,200	600	0	600	2%	0%		0		
MV Trench Excavation	LF	3,200	600	0	600	5%	0%		0		
MV Cable Splices	ea.	320	60	0	60	3%	0%		0		
Fiber Optic Installation	ea.	3,200	600	0	600	5%	0%		0		
Fiber Optic Terminations / Splices	ea.	320	60	0	60	5%	0%		0		
Fiber Optic Testing	ea.	64	12	0	12	8%	0%		0		
MV Cable Installation & Backfill	LF	3,200	600	0	600	15%	0%		0		
Bores	ea.	160	30	0	30	15%	0%		0		
MV Terminations	ea.	160	30	0	30	5%	0%		0		
Junction Boxes	ea.	80	15	0	15	5%	0%		0		
PMT Vault Installation	ea.	32	6	0	6	7%	0%		0		
PMT Installation	ea.	32	6	0	6	2%	0%		0		
PMT Testing	ea.	32	6	0	6	15%	0%		0		
PD / VLF Testing	ea.	16	3	0	3	5%	0%		0		
Grounding System Testing	ea.	32	6	0	6	3%	0%		0		
CREWS: 0 HEADCOUNT: 0											
WTG Erection & Mechanical Overall Completion											
				0 Turbines	24 Turbines	100%	0%				
Switchgear or DTE	ea.	24	24	0	24	10%	0%		0		
Base Section Erected	ea.	24	24	0	24	10%	0%		0		
Lower Mid Section Erected	ea.	24	24	0	24	5%	0%		0		
Upper Mid Section Erected	ea.	24	24	0	24	5%	0%		0		
Grouting	ea.	24	24	0	24	10%	0%		0		
Top Section Erected	ea.	24	24	0	24	10%	0%		0		
Rotor Assembly	ea.	24	24	0	24	10%	0%		0		
Nacelle Installation	ea.	24	24	0	24	10%	0%		0		
Hub-Blades Set Installation	ea.	24	24	0	24	10%	0%		0		
Tower Wiring	ea.	24	24	0	24	10%	0%		0		
Mechanical Walkdown (Punch list issued)	ea.	24	24	0	24	10%	0%		0		
CREWS: 0 HEADCOUNT: 0											
Turbine Commissioning											
				0 Turbines	24 Turbines	100%	0%				
Pre-Commissioned (Cold)	ea.	24	24	0	24	30%	0%		0		
Turbine Commissioned On Grid	ea.	24	24	0	24	40%	0%		0		
Reliability Test Certificate Received	ea.	24	24	0	24	30%	0%		0		
CREWS: 0 HEADCOUNT: 0											
Commissioning											
				100% Remain	100%	0%					
HV Connection Lines	%	100%	100%	0.0%	100%	8.0%	0%		0.0%		
Delivery Substation	%	100%	100%	0.0%	100%	8.0%	0%		0.0%		
Step-Up Substation	%	100%	100%	0.0%	100%	25.5%	0%		0.0%		
ICT Communication System	%	100%	100%	0.0%	100%	8.0%	0%		0.0%		
SCADA System	%	100%	100%	0.0%	100%	10.0%	0%		0.0%		
Circuits Commissioning	%	100%	100%	0.0%	100%	24.0%	0%		0.0%		
Transmission Line	%	100%	100%	0.0%	100%	10.0%	0%		0.0%		
Completion and Performance Test	%	100%	100%	0.0%	100%	6.5%	0%		0.0%		
CREWS: 0 HEADCOUNT: 0											



Friday, June 28, 2019



WHITNEY HILL WIND FARM

24 WTG's
21 GE 2.8 MW & 3 GE 2.3 MW
65 MW Capacity



Substantial Completion

Friday, November 15, 2019

COD

Monday, December 23, 2019

NON CONFORMITY REGISTER

Identification		NC Opening				NC Resolution		
#	Type	Detected by (Unit)	Date of Detection	Supplier	NC Description	Action	Expected date for closure	Resolution validated by


Contractor	MECHANICAL COMPLETION AND COMMISSIONING STATUS					0%
	Stage	UNIT	TOTAL QTY	COMPLETED	PROGRESS	
	WTG - Circuits (Collection Line)	ea.	3	0	0%	
	WTG - Walk Down (punch list issued)	ea.	24	0	0%	
	WTG MCC (Issued by BoP Contractor)	ea.	24	0	0%	
	WTG MCC (Signed by BoP Contractor)	ea.	24	0	0%	
	WTG MCC (Issued/signed by Supplier)	ea.	24	0	0%	
	WTG Pre-Commissioning	ea.	24	0	0%	
	WTG Commissioning	ea.	24	0	0%	
	WTG Reliability Run Test Finalized	ea.	24	0	0%	
	Substation Commissioning	%	1	0	0%	
	First Synchronization	ea.	1	0	0%	
	Additional Capacity Declaration	ea.	1	0	0%	

COMPLETION CERTIFICATES STATUS				
Certificate Name	Total	Signed	Remaining	Progress
Turbine Delivery Completed	24	0	24	0%
Foundation Completion	24	0	24	0%
WTG Mechanical Completion	24	0	24	0%
Reliability Test	24	0	24	0%
Commissioning	24	0	24	0%
UGCS Completion	3	0	3	0%
Substation Mechanical Completion	1	0	1	0%
O&M Building Completion	1	0	1	0%
Substantial BoP Completion	1	0	1	0%
Substantial Substation Completion	1	0	1	0%
Final Completion	1	0	1	0%

WEATHER DELAYS	NUMBER OF SHIFTS CONSIDERED AS "WEATHER DELAY DAY"			
	Wind	Rain / Snow / Fog	Lightning	Ice
BoP Civil	1	1	0	0
Turbine Erection	0	0	1	0
WTG Deliveries	0	0	0	0
Substation	0	0	0	0
Transmission Line	0	0	0	1
Commissioning	0	0	0	0

PREVIOUS DAY ON-SITE HEAD COUNT	
Enel Green Power	0
BoP Contractor and Subs	0
Turbine Supplier	0
Substation Contractor and Subs	0
TOTAL	0

SITE GPS COORDINATES	
O&M Building	
LAT	
LONG	
Substation	
LAT	
LONG	
POI	
LAT	
LONG	

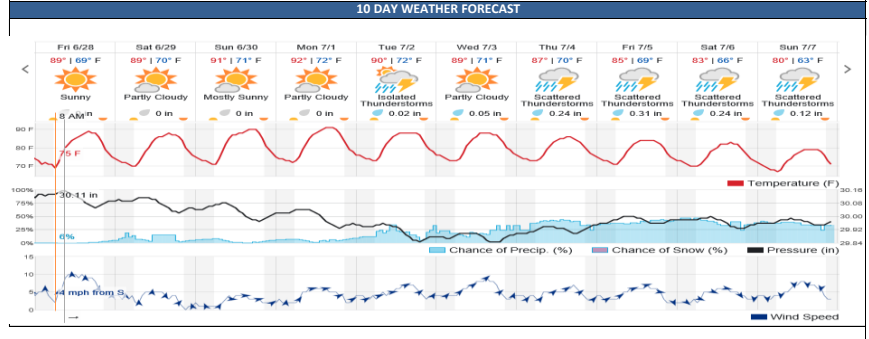

Total Project Hours	0
----------------------------	----------
