



Tuesday, September 11, 2018  
PLAN OF THE DAY (PoD)

HillTopper Wind Farm  
74 WTG's  
GE 2.50 MW  
185 MW Capacity



Substantial Completion Wednesday, October 31, 2018  
COD Saturday, December 1, 2018

**TODAY'S WEATHER FORECAST**


Conditions	SUNNY	Wind Direction	L&V	Wind Speed	Light & Variable	Dew Point	43 °F	Temperature	77 °F	53 °F	Humidity	75%	Precipitation	0%
------------	-------	----------------	-----	------------	------------------	-----------	-------	-------------	-------	-------	----------	-----	---------------	----

**DAILY ROAD CLOSURES/BLOCKAGES**

Please help keep our guys safe and watch speeds in marked construction areas.

TUESDAY, 9/11	Extended Road Closure For Pulverization and Cement Stabilization will be on 1075th/1039th from A01 to CH 12. This Road Closure will Extend Through Tuesday, 9/11.
TUESDAY, 9/11	Extended Road Closure For Pulverization and Cement Stabilization will be on 400th from 1400th to 1500th. This Road Closure will Extend Through Wednesday, 9/12.
TUESDAY, 9/11	Extended Road Closure For Pulverization and Cement Stabilization will be on 300th from H07 to 1750th. This Road Closure will Extend Through Thursday, 9/13.
TUESDAY, 9/11	Extended Road Closure For Pulverization and Cement Stabilization will be on 400th from H04 to 1750th. This Road Closure will Extend Through Thursday, 9/13.
TUESDAY, 9/11	Extended Road Closure For Tilling and Compaction will be on 1500th from G03 to 400th. This Road Closure will Extend Through Thursday, 9/13.
TUESDAY, 9/11	Extended Road Closure For Tilling and Compaction will be on 1400th from IL 54 to 500th. This Road Closure will Extend Through Thursday, 9/13.
TUESDAY, 9/11	Extended Road Closure For Tilling and Compaction will be on 500th from E02 to 1375th. This Road Closure will Extend Through Thursday, 9/13.
TUESDAY, 9/11	Extended Road Closure For Tilling and Compaction will be on 1375th from 500th to 600th. This Road Closure will Extend Through Thursday, 9/13.
TUESDAY, 9/11	Extended Road Closure For Pulverization will be on 600th east of 1375th. This Road Closure will Extend Through Thursday, 9/13.
TUESDAY, 9/11	Extended Road Closure for Jump Bridge Installation on 1039th from A01 to 900th. This Road Closure will Extend Through Saturday, 9/15.
TUESDAY, 9/11	Extended Road Closure For Pulverization and Cement Stabilization will be on 950th from A02/3 to CH 10. This Road Closure will Extend Through Monday, 9/17.
TUESDAY, 9/11	Extended Road Closure For Pulverization and Cement Stabilization will be on 1150th from 480th to E08. This Road Closure will Extend Through Monday, 9/17.

**Extended Road Closure Notice  
(For Public Road Works)**

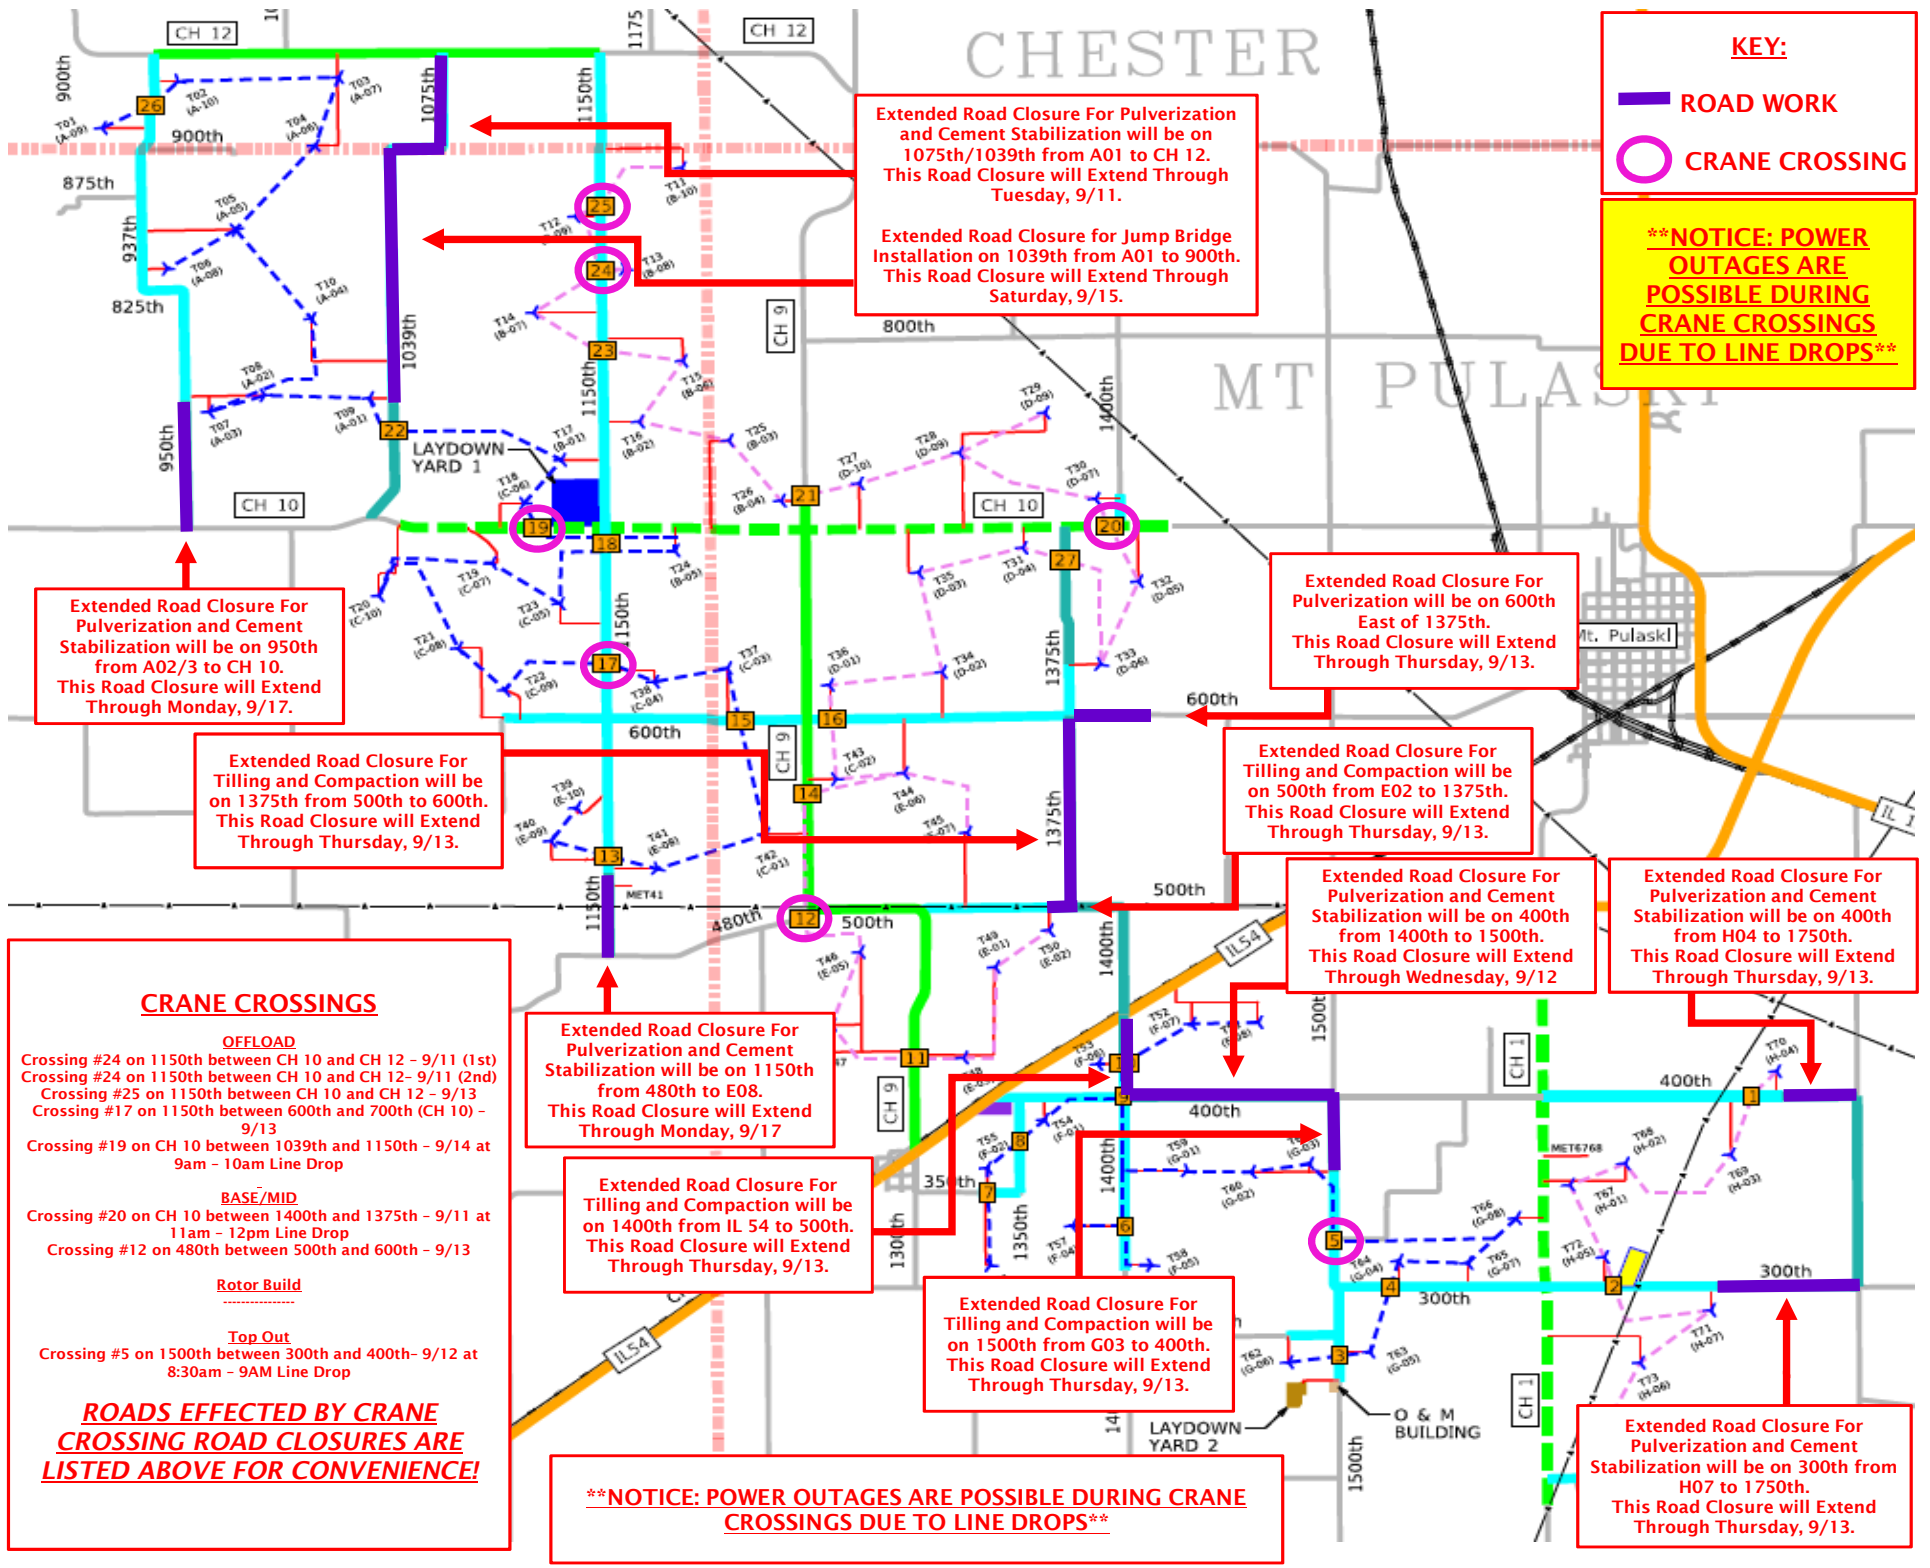

Please contact the following people if there are any questions.  
 Daniel Sheehan - dsheehan@swiftcurrentenergy.com  
 Antonio Bombaci - antonio.bombaci@enel.com  
 Moris Schiavoni - moris.schiavoni@enel.com
