



Wednesday, September 5, 2018
PLAN OF THE DAY (PoD)

HillTopper Wind Farm
 74 WTC's
 GE 2.50 MW
185 MW Capacity



Substantial Completion	Wednesday, October 31, 2018
COD	Saturday, December 1, 2018

TODAY'S WEATHER FORECAST


Conditions	Sunny	Wind Direction	S	Wind Speed	5-10 MPH	Dew Point	49 -F	Temperature	91 'F	70 'F	Humidity	65%	Precipitation	20%
------------	-------	----------------	---	------------	----------	-----------	-------	-------------	-------	-------	----------	-----	---------------	-----

DAILY ROAD CLOSURES/BLOCKAGES


Please help keep our guys safe and watch speeds in marked construction areas.

**Extended Road Closure Notice
 (For Public Road Works)**


Wednesday 9/5	Extended Road Closure For Cement Stabilization will be on 1400th from F05 to 400th. This Road Closure will Extend Through Wednesday, 9/5.
Wednesday 9/5	Extended Road Closure For Pulverization and Cement Stabilization will be on 300th from H03 to 1750th. This Road Closure will Extend Through Thursday, 9/6.
Wednesday 9/5	Extended Road Closure For Pulverization and Cement Stabilization will be on 400th from H04 to 1750th. This Road Closure will Extend Through Friday, 9/8
Wednesday 9/5	Extended Road Closure For Pulverization and Cement Stabilization will be on 400th from 1400th to 1500th. This Road Closure will Extend Through Friday, 9/8.

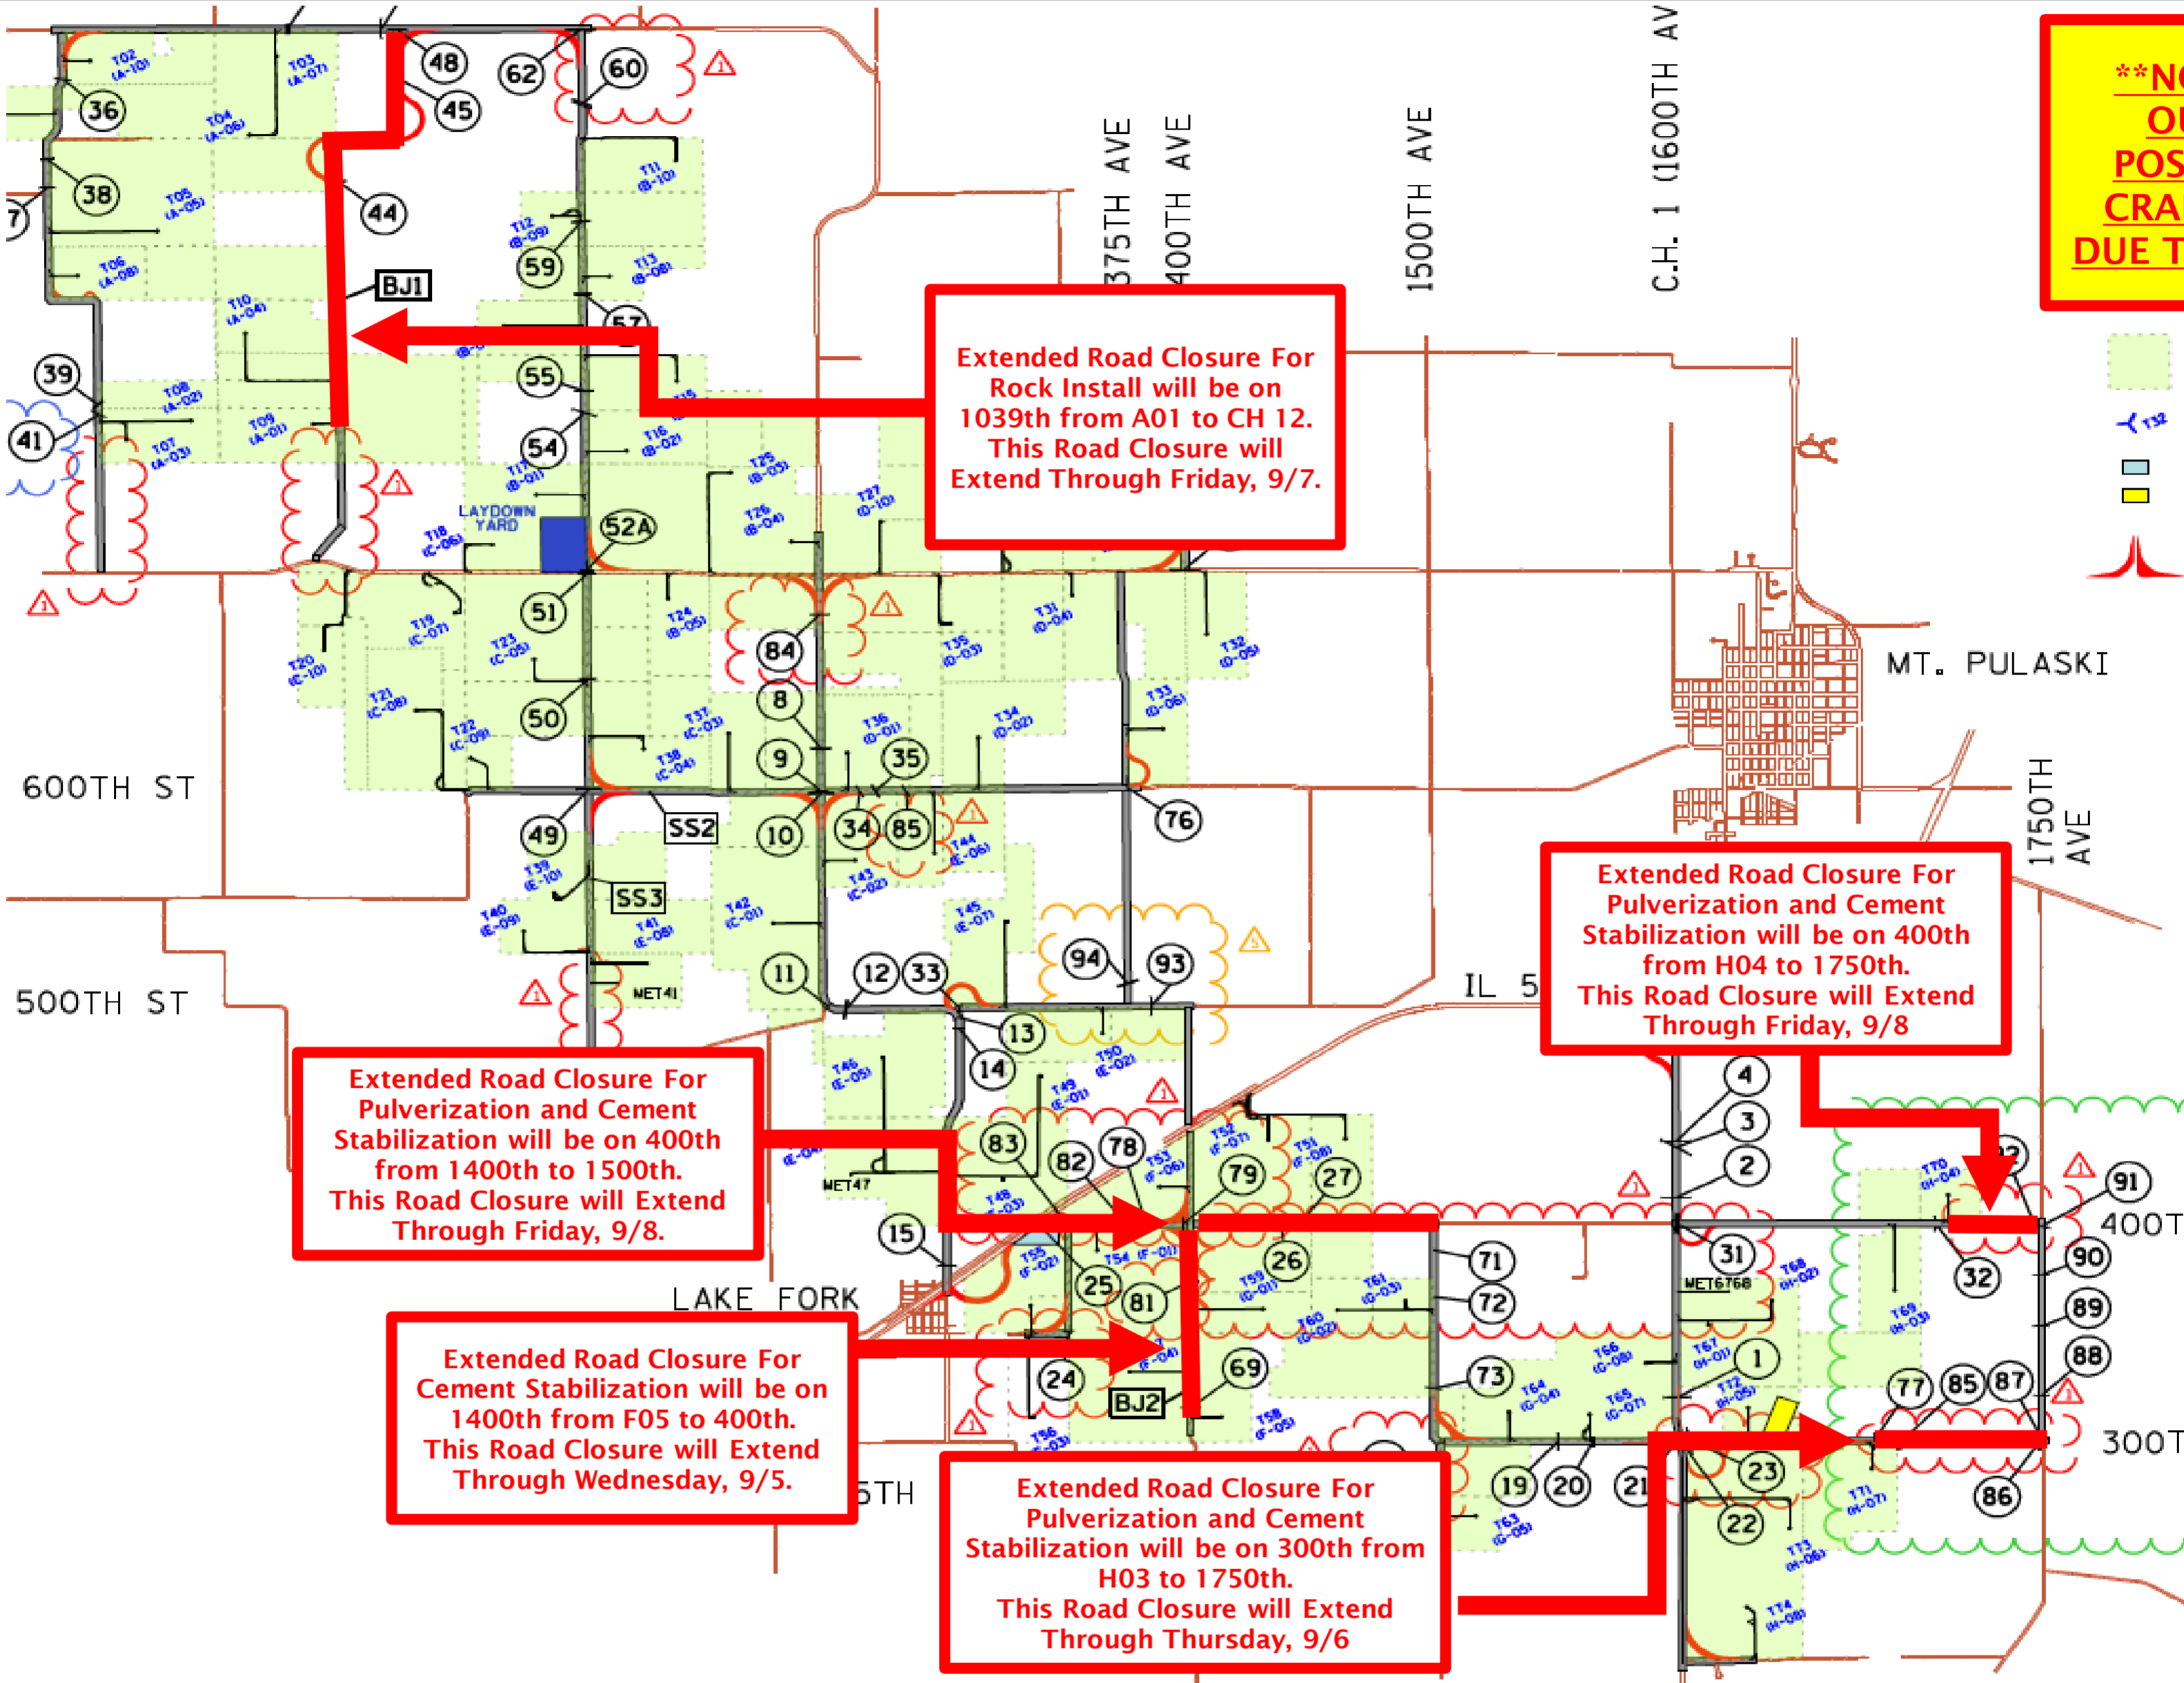

****NOTICE: POWER OUTAGES ARE POSSIBLE DURING CRANE CROSSINGS DUE TO LINE DROPS****

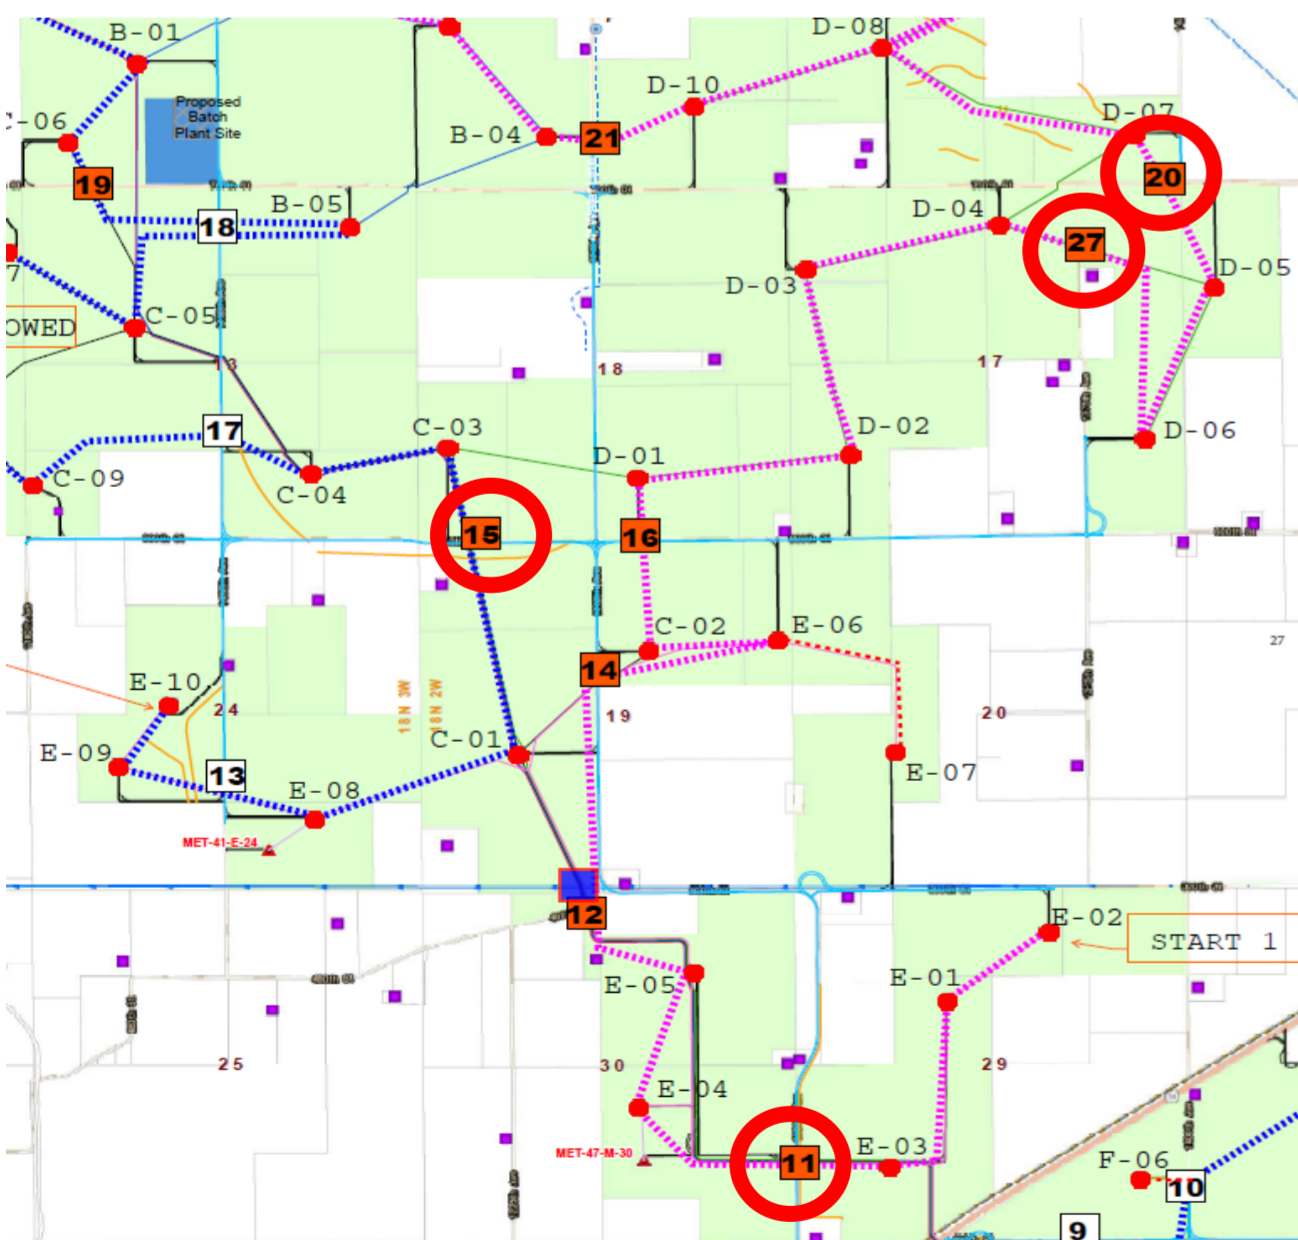

****NOTICE: POWER OUTAGES ARE POSSIBLE DURING CRANE CROSSINGS DUE TO LINE DROPS****

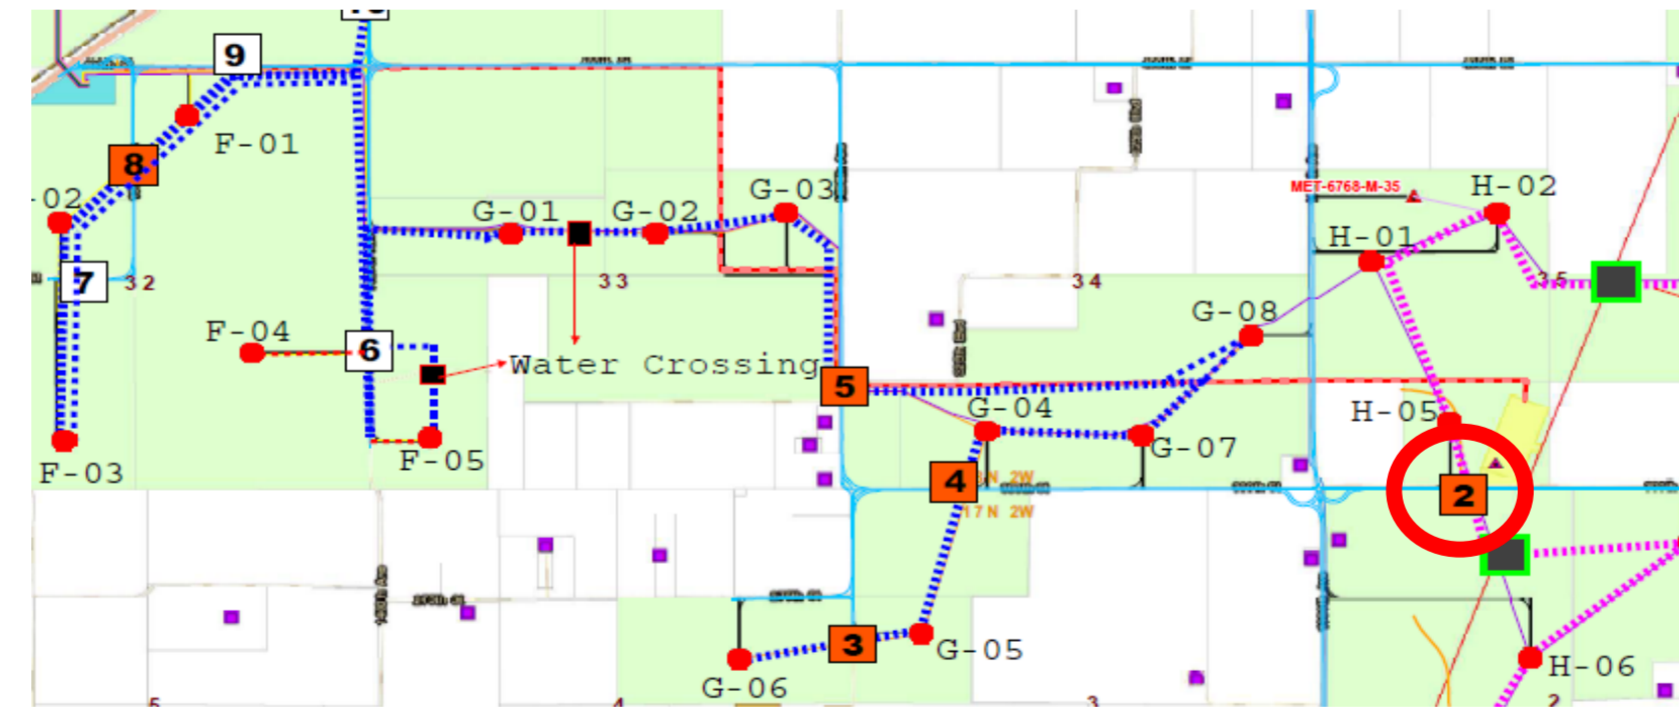

- CRANE CROSSINGS**
- OFFLOAD**
 Crossing #15 - 9/6/18 @ 9AM - 10AM
 Line Drop
 - BASE/MID**
 Crossing #27 - 9/5/18 at 10AM -
 Line Drop @ 11AM
 - Rotor Build**
 Crossing #11 - 9/6/18 at 12PM - 1PM
 Line Drop
 - Top Out**
 Crossing #20 - 9/7/18 at 12PM - 1PM
 Line Drop

Please contact the following people if there are any questions.
 Daniel Sheehan - dsheehan@swiftcurrentenergy.com
 Antonio Bombaci - antonio.bombaci@enel.com
 Moris Schiavoni - moris.schiavoni@enel.com
