EIMS | ENVIRONMENTAL IMPACT MANAGEMENT SERVICES

T 011 789 7170 E info@eims.co.za W www.eims.co.za

APRIL 2024 MONTHLY ECO AUDIT REPORT

IMPOFU CLUSTER WIND ENERGY FACILITY

DEA Reference Numbers:

Impofu North Wind Energy Facility: 14/12/16/3/3/2/1102
Impofu West Wind Energy Facility: 14/12/16/3/3/2/1103
Impofu East Wind Energy Facility: 14/12/16/3/3/2/1104
Buffer Yard and Concrete Batching Plant: 14/12/16/3/3/1/2776



DOCUMENT DETAILS

EIMS REFERENCE:	1594
DOCUMENT TITLE:	April 2024 Monthly ECO Audit Report

DOCUMENT CONTROL

	NAME	SIGNATURE	DATE
COMPILED:	Bulelwa Runeyi	Sent Electronically	2024/04/22
CHECKED:	Sikhumbuzo Mahlangu	Sent Electronically	2024/05/10
AUTHORIZED:	Liam Whitlow	Sent Electronically	2024/05/10

REVISION AND AMENDMENTS

REVISION DATE:	REV #	DESCRIPTION
2024/04/22	ORIGINAL DOCUMENT	Draft ECO Report
2024/05/13	REVISION 1	Final ECO Report

This document contains information proprietary to Environmental Impact Management Services (Pty) Ltd. and as such should be treated as confidential unless specifically identified as a public document by law. The document may not be copied, reproduced, or used for any manner without prior written consent from EIMS. Copyright is specifically reserved.

Table of Contents

1 INTRODUCTION 4
1.1 DETAILS OF THE HOLDER 4
1.2 BRIEF PROJECT DESCRIPTION 5
1.3 PROJECT PROGRESS 7
2 DETAILS OF THE ECO 8
2.1 EXPERTISE OF THE ECO 8
2.2 DECLARATION OF INDEPENDENCE 9
3 SCOPE, PURPOSE AND OBJECTIVE OF THE AUDIT 9
4 AUDIT METHODOLOGY 10
4.1 PROCEDURE FOR THE AUDIT 10
4.2 EVALUATION CRITERIA USED DURING THE AUDIT 10
4.3 DOCUMENTATION REVIEW 10
4.4 SITE ASSESSMENT 13
5 RESULTS OF THE AUDIT / LEGAL COMPLIANCE 13
5.1 COMPLIANCE SUMMARY 13
5.2 GOOD COMPLIANCES 14
5.3 AREAS OF CONCERN 16
5.4 NON-COMPLIANCES 17
5.5 NON-COMPLIANCE REPORTS 19
5.6 INCIDENTS 19
5.7 COMPLAINTS 19
5.8 STATUS OF NON-COMPLIANCES REPORTED DURING PREVIOUS REPORTING PERIODS 20
6 CONCLUSION 22
7 ASSUMPTIONS AND LIMITATIONS 22

List of Tables

Table 1: Details of the holder. 4
Table 2: List of Good Compliances recorded during this reporting period. 14
Table 3: Environmental Non-Compliances raised during the current reporting period. 17
Table 4: Environmental Non-Compliances raised during the previous reporting period. 20
Table 5: Summary of observations noted. 22

Figures

Figure 1: Impofu Cluster boundaries 6
Figure 2: Drip tray placed under parked water bowser. 8

Figure 3: Toilets available in all working areas. 8
Figure 4: Stormwater pipes installed to avoid soil erosion. 8
Figure 5: Environmentally sensitive areas signage erected near watercourses and wetlands to restrict work in proximity of the areas. 8
Figure 6: Water abstracted from registered Oyster Bay Dam. 12
Figure 7: Registered boreholes installed. 12
Figure 8: Summary of compliance with the requirements of the EA. 13
Figure 9: Summary of compliance with the requirements of the EMPr. 13
Figure 10: Temporary fence and appropriate signage erected around a heritage site near WTGE19, turn-around point RE25 and RE22 14
Figure 11: Storage area neat and clean. 14
Figure 12: Stockpiles do not exceed 2 m in height. 15

List of Abbreviations

Abbreviation	Item
DEA	Department of Environmental Affairs
DFFE	Department of Forestry, Fisheries and the Environment
EA	Environmental Authorisation
ECO	Environmental Control Officer
EO	Environmental Officer
EGP	Enel Green Power
EIMS	Environmental Impact Management Services (Pty) Ltd
EMPr	Environmental Management Programme
GA	General Authorisation
I&AP	Interested and Affected Party
NC	Non-Compliance
NCR	Non-Compliance Report
NMBMM	Nelson Mandela Bay Metropolitan Municipality
OHL	Overhead Line
MPRDA	Mineral and Petroleum Resources Development Act

Abbreviation	Item
WF	Wind Farm
WTG	Wind Turbine Generator

Definitions

Term	Definition
Non-compliance (NC)	Instances where a provision of environmental legislation (national, provincial, or local) and/or condition of an environmental approval (for example, environmental authorisation, water use licence, waste licence, licence in terms of the National Forests Act) or any other legal document issued in terms of environmental legislation is contravened. For the purpose of the monthly ECO audits, it will include contraventions to the provisions of the EA and EMPr.
Incident	Any unplanned event that could, or does, result in harm, damage, and/or environmental pollution or degradation or gives rise to an accident or has the potential to lead to an accident.
Incident management	Incident management is an integral function of risk management and is aimed at reducing the impact of incidents, enabling corrective action to be taken and changed practice to be introduced. It also allows for learning from the incidents that have occurred to prevent similar incidents from happening or to mitigate their impact. This includes the effective communicating, reporting, measurement, recording and investigation of incidents.
NEMA section 30 incident	"Incident" means an unexpected, sudden and uncontrolled release of a hazardous substance, including from a major emission, fire or explosion, that causes, has caused or may cause significant harm to the environment, human life or property.

1 INTRODUCTION

Red Cap Impofu (Pty) Ltd was granted Environmental Authorisations (EAs) for construction of the three wind farms and associated infrastructure (i.e. Impofu North Wind Farm with DEA reference number: 14/12/16/3/3/2/1102; Impofu West Wind Farm with DEA reference number: 14/12/16/3/3/2/1103; Impofu East Wind Farms with DEA reference number: 14/12/16/3/3/2/1104) near Oyster Bay within Koukamma and Kouga Local Municipalities in the Eastern Cape. These Wind Farms (WF) are referred to as Impofu wind farms (Impofu Cluster).

The consolidated site of the Impofu Cluster is boarded by the operational Tsitsikamma Community Wind Farm to the west, the Gibson Bay Wind Farm to the south-west, the Oyster Bay Wind Farm and the Kouga Wind Farm to the south-east and extend over approximately 12 000 hectares (ha). More specifically, the Impofu East Wind Farm falls in the south-eastern extent of the site, with the Impofu West Wind Farm immediately west of it, with the Impofu North Wind Farm located to its north.

Ancillary infrastructure associated with the Impofu Cluster includes but is not limited to underground and above ground cabling between project components, with each Impofu WF having its own substation, foundations to support turbine towers, hardstands to support cranes at each turbine, permanent operations/maintenance buildings, temporary construction office and workshop areas. Service and access roads will be constructed in addition to upgrading existing roads, with the relevant stormwater infrastructure and gates constructed as required. Formal laydown areas for the construction period, containing temporary maintenance and storage buildings along with guard cabins will also be established. A buffer yard with turbine assembly will be established within the Impofu West boundary but will service the entire cluster. Concrete tower technology will be used for the wind turbines. Enel Green Power (Pty) Ltd (EGP) appointed Environmental Impact Management Services (Pty) Ltd (EIMS) to provide the services of the independent ECO.

This report provides details of the outcome of an environmental compliance audit for the month of April 2024 for the development of three (3) Wind Energy Facilities referred to as the Impofu Wind Cluster and associated infrastructure near Oyster Bay in the Eastern Cape.

1.1 DETAILS OF THE HOLDER

Details of the holder are summarised in Table 1 below.

Table 1: Details of the holder.

Company Name	Red Cap Impofu (Pty) Ltd.
Company Registration	Mr Lance Blaine
Head Office Physical Address	2017/118197/07
Head Office Telephone Number	Unit 2B, Mainstream Centre, Cape Town, 7806
Head Office Fax Number	(021) 790 1392
Head Office Contact Person	Mr Lance Blaine
Operations Physical Address	Impofu Wind Farm Cluster
Operations Telephone number	079 434 9559
Operations Contact Person	Mr Zishaan Khan

1.2 BRIEF PROJECT DESCRIPTION

The Impofu Cluster has a combined electrical generation capacity of approximately 333 MW. Each of these Wind Farms underwent separate environmental authorisation processes. Details of each wind farm comprising the cluster are noted below.

Impofu North

The Impofu North Wind Farm is located predominantly within the Kouga Local Municipality but also in the Koukamma Local Municipality (both within the Sarah Baartman District Municipality). The Impofu North site is centred on 34°2'54"S and 24°32'24.6"E and is approximately 16 kilometres (km) north-west of Oyster Bay as taken from the centre point. The Impofu North Wind Farm footprint straddles the N2 National Road and R102 Main Road. Initially the Wind Farm was authorised to construct Impofu North Wind Farm, a 182 MW Wind Farm comprised of up to 26 wind turbines. Following various assessments and new technologies becoming available, this was revised and is now 112.1 MW through 19 turbines.

Impofu East

The Impofu East Wind Farm is located entirely within the Kouga Local Municipality, within the Sarah Baartman District Municipality. The Impofu East site is centred on 34°7'37.9"S and 24°36'28.7"E. It is approximately 18 kilometres (km) south-west of Humansdorp, and approximately 6 km north-west of the town of Oyster Bay from the centre point of the site (700 m away at its closest point). The Impofu East Wind Farm is situated to the south of the N2 National Road and R102 Main Road. Initially the Wind Farm was authorised to construct Impofu East Wind Farm, a 189 MW Wind Farm comprised of up to 27 wind turbines. As above, this was revised and is now 112.1 MW through 19 turbines.

Impofu West

The Impofu West Wind Farm is located entirely within the Kouga Local Municipality, within the Sarah Baartman District Municipality. The Impofu West site is centred on 34°5'28" South latitude and 24°32'53" East longitude and is approximately 14 kilometres (km) north-west of Oyster Bay as taken from the centre point. Initially the Wind Farm was authorised to construct Impofu West Wind Farm, a 168 MW Wind Farm comprised of up to 24 wind turbines. As above, this was revised and is now 112.1MW through 19 turbines. (Refer to figure 1 for the Impofu Cluster boundaries).

Authorisations, Permit and or Management Plans

The "Impofu Cluster" wind farms are located near Humansdorp of the Eastern Cape province and are split into three distinct areas known as Impofu North, West and East.

The below authorisations were obtained for the aforementioned:

- Impofu Wind Farm Cluster:
    - NEMA
        - Impofu East EA – 14/12/16/3/3/2/1103 (with amendments);
        - Impofu North EA – 14/12/16/3/3/2/1102 (with amendments);
        - Impofu West EA – 14/12/16/3/3/2/1104 (with amendments);
        - Impofu Cluster – Buffer yard (14/12/16/3/3/1/2776) (situated at West).
    - NWA
        - Impofu East GA Section 21(a), (c) and (i);
        - Impofu North GA Section 21(a), (c) and (i); and
        - Impofu West GA Section 21(a), (c) and (i).

Additional to the above authorisations, EMPr's have been approved for each of the authorisations.

Other permits (such as biodiversity) may also apply. Refer to section 4.1 for additional permits.

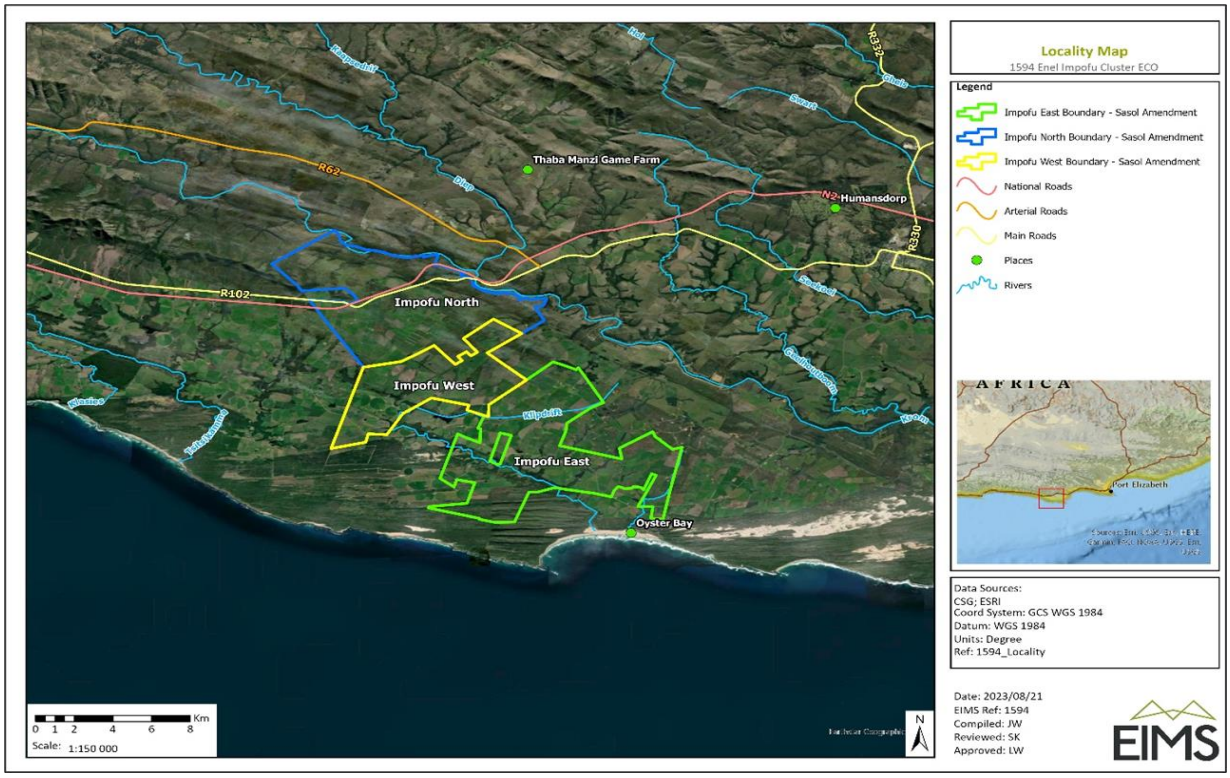


Figure 1: Impofu Cluster boundaries

The112.1MW Impofu North Wind Farm will comprise of the following infrastructure:

- Turbines: Up to 19 turbines with a hub height of 120m, and rotor diameter of 163m, the minimum tip height (ground clearance) will be at least 38.5m:
- Crane hard stands: One per turbine, with a permanent hardstand 40m x 50m which will remain for maintenance purposes;
- Access and internal roads: The internal gravel roads will be approximately 6m wide with potential side drains. Some sections of these roads would need to the temporary widened up to 12m during construction;
- On-site substation: Each substation is approximately 150 x 75m (11 250m^2) which will occupy the area for operation and maintenance;
- Cables: Each turbine will be connected to the substation via medium voltage cables (~33kV lines). Where feasible the cables will be laid underground in trenches, generally running alongside existing or proposed new internal roads. Where burying of cables is not possible due to technical, geological, environmental or topographical constraints, then burying of cables is not possible due to technical, geological, environmental or topographical constraints, then overhead power lines will be erected;
- Permanent Operational & Maintenance (O&M) buildings: The substation area would house buildings or areas for control, operation, workshop and storage: and,
- Laydown area and site camp: The temporary laydown areas will be approximately 161 200m^2 and the permanent area 52 000m^2 and the temporary site camp of approximately 15,000m^2. An additional 1,000m^2 will be temporarily required for concrete batching.

The 112.1MW Impofu West Wind Farm will comprise of the following infrastructure:

- Turbines: Up to 19 turbines with a hub height of 120m, and rotor diameter of 163m, the minimum tip height (ground clearance) will be at least 38.5m:
- Crane hard stands: One per turbine, with a permanent hardstand 50m x 40m which will remain for maintenance purposes;
- Access and internal roads: The internal gravel roads will be approximately 6m wide with potential side drains. Some sections of these roads would need to the temporary widened up to 12m during construction;



- On-site substation: Each substation is approximately 150 x 75m (11 250m^2) which will occupy the area for operation and maintenance;
- Cables: Each turbine will be connected to the substation via medium voltage cables (~33kV lines). Where feasible the cables will be laid underground in trenches, generally running alongside existing or proposed new internal roads. Where burying of cables is not possible due to technical, geological, environmental or topographical constraints, then burying of cables is not possible due to technical, geological, environmental or topographical constraints, then overhead power lines will be erected;
- Permanent Operational & Maintenance (O&M) buildings: The substation area would house buildings or areas for control, operation, workshop and storage: and,
- Laydown area and site camp: The temporary laydown areas will be approximately 148 800m^2 and the permanent area 48 000m^2 and the temporary site camp of approximately 15,000m^2. An additional 1,000m^2 will be temporarily required for concrete batching.

The 112.1MW Impofu East Wind Farm will comprise of the following infrastructure:

- Turbines: Up to 19 turbines with a hub height of 120m, and rotor diameter of 163m, the minimum tip height (ground clearance) will be at least 38.5m:
- Crane hard stands: One per turbine, with a permanent hardstand 40m x 50m which will remain for maintenance purposes;
- Access and internal roads: The internal gravel roads will be approximately 6m wide with potential side drains. Some sections of these roads would need to the temporary widened up to 12m during construction;
- On-site substation: Each substation is approximately 150 x 75m (11 250m^2) which will occupy the area for operation and maintenance;
- Cables: Each turbine will be connected to the substation via medium voltage cables (~33kV lines). Where feasible the cables will be laid underground in trenches, generally running alongside existing or proposed new internal roads. Where burying of cables is not possible due to technical, geological, environmental or topographical constraints, then burying of cables is not possible due to technical, geological, environmental or topographical constraints, then overhead power lines will be erected;
- Permanent Operational & Maintenance (O&M) buildings: The substation area would house buildings or areas for control, operation, workshop and storage: and,
- Laydown area and site camp: The temporary laydown areas will be approximately 167 400m^2 and the permanent area 54 000m^2 and the temporary site camp of approximately 15,000m^2. An additional 1,000m^2 will be temporarily required for concrete batching.

1.3 PROJECT PROGRESS

The project has two (2) contractors, Power Construction (appointed for civil works) and Brand Besamandla (appointed for electrical works). Only Power construction is working on site. Main activities are on Impofu North and West then minor activities on East. The audit was conducted on the 22nd of April 2024. Activities currently ongoing on site includes clearing and grabbing, excavations for turbine foundation, stripping in road 8 and 9 at West, relocation of existing services, i.e. fences and water troughs, borehole installation, erection of storage dams, and maintenance of access roads. Only activities done on Impofu East include fencing and installation of stormwater pipe for bypass road to WTG E13 and 14.



Figure 2: Drip tray placed under parked water bowser.



Figure 3: Toilets available in all working areas.



Figure 4: Stormwater pipes installed to avoid soil erosion.



Figure 5: Environmentally sensitive areas signage erected near watercourses and wetlands to restrict work in proximity of the areas.

2 DETAILS OF THE ECO

As per the issued EAs, an experienced independent Environmental Control Officer (ECO) with experience in the environmental management field was appointed for the construction phase of the development as required in terms of Condition 25 of the EAs. EGP appointed Environmental Impact Management Services (Pty) Ltd (EIMS) to provide the services of the independent ECO. The ECO audit was undertaken by Bulelwa Runeyi from EIMS.

2.1 EXPERTISE OF THE ECO

Bulelwa Runeyi has a National Diploma in Environmental Management with an excess of 10 years' experience in the Environmental Management field. She has completed a short course in Environmental Law with the University of Pretoria. She is a registered Environmental Assessment Practitioner (EAP) with the Environmental Assessment Practitioners Association of South Africa (EAPASA). After graduating, Bulelwa worked in a private company as an Environmental Officer where she gained experience in environmental education and conducting environmental awareness campaigns in schools and communities. She further acquired training in stakeholder engagements and peer coaching on environmental conservation. She also has experience in conducting Environmental Impact Assessments, Water Use License Applications, Public Participation Coordination,

development of Environmental Management Programmes, and conducting independent environmental compliance audits.

2.2 DECLARATION OF INDEPENDENCE

*I, **Bulelwa Runeyi**, declare that –*

- *I act as the independent Environmental Control Officer;*
- *I will perform the work relating to the ECO audits in an objective manner, even if this results in views and findings that are not favourable to the Client;*
- *I declare that there are no circumstances that may compromise my objectivity in performing such work;*
- *I have expertise in conducting environmental audits, including knowledge of the environmental Acts, regulations and any guidelines that have relevance to the audited operations;*
- *I will comply with the relevant Acts, regulations and all other applicable legislation;*
- *I have no, and will not engage in, conflicting interests in the audit process; and*
- *I realise that a false declaration is an offence in terms of regulation 48 and is punishable in terms of section 24F of the NEMA.*

I do not have and will not have any vested interest (either business, financial, personal or other) in the audit other than remuneration for work performed.

Signature: 

3 SCOPE, PURPOSE AND OBJECTIVE OF THE AUDIT

The scope of the audit is to assess compliance with the conditions of the Impofu Wind Farms (North, West and East) and their associated infrastructure EA/EMPr as well as related permits and licences near Oyster Bay in the Eastern Cape Province. The EMPr dated 17 May 2023 was approved was approved by DFFE on the 13th of June 2023 as part of the EA for Impofu Wind Farms. The purpose of the audit is to ensure compliance with the requirements of the EMPr which requires monthly compliance monitoring of the EMPr during the construction period. The objective of the audit is to determine and monitor the level of compliance of the License Holder with the provisions of the requisite EA and EMPr, related permits as well as licences. This report is prepared in accordance with Appendix 7 of the 2014 EIA Regulations (as amended). The objective of the environmental audit report is to:

- report on –
  - the level of compliance with the conditions of the EA and the EMPr, and where applicable, the closure plan; and
  - the extent to which the avoidance, management and mitigation measures provided for in the EMPr, and where applicable, the closure plan achieves the objectives and outcomes of the EMPr, and closure plan.
- identify and assess any new impacts and risks as a result of undertaking the activity.
- evaluate the effectiveness of the EMPr, and where applicable, the closure plan.
- identify shortcomings in the EMPr, and where applicable, the closure plan; and
- identify the need for any changes to the avoidance, management and mitigation measures provided for in the EMPr, and where applicable, the closure plan.

4 AUDIT METHODOLOGY

4.1 PROCEDURE FOR THE AUDIT

Regular audits are conducted in accordance with the principles and processes outlined in SANS 19011: 2012 Edition 2: Guidelines for Auditing Management Systems. The audit focused on the following elements of the project with respect to the EA (DEA Ref: 14/12/16/3/3/2/1102, 14/12/16/3/3/2/1103 and 14/12/16/3/3/2/1104) as well as the updated and approved EMPr for the Impofu Wind Farms and associated infrastructure dated 17 May 2023; relevant environmental legislations, as well as environmental method statements. Audit was also conducted for the Water Use Authorisation (Ref Nos.: WU9784, WU20735, WU14968, WU20748, WU15014, WU20736, and WU15001) in terms of the National Water Act 36 of 1998 section 22 (1) (a) (iii).

During the audit, the ECO requested the following information:

- EA, EMPr, permits, licences, all other relevant authorisations and approvals.
- Environmental management monitoring such as water use registers, test analysis, noise and dust monitoring (if any).
- Pre-Construction requirements such as site establishment requirements/method statements and layout plan.
- Training requirements such as inductions, and awareness training registers.
- Incident reports and incident registers.
- Compliant registers.
- Waste management manifests, and
- Contractor's EO weekly/ weekly site inspection reports.

4.2 EVALUATION CRITERIA USED DURING THE AUDIT

The evaluation criteria for compliance scoring was based on a pre-determined scoring system. Each condition of the EA and EMPr was weighted equally in order to determine a compliance score. The scoring criteria used during the audit are as follows:

- Full-Compliance: Indicating that the condition was fully complied with and provided with a compliance score of 4.

- Partial-Compliance: Indicating that the condition has not been fully complied with and that additional measures are required to obtain full compliance. Partial compliances were provided with a compliance score of 2.

- Non-Compliance: Indicting that the condition has not been complied with and provided with a compliance score of 0.

- Not Applicable (N/A): Indicating that the condition is not currently applicable. Not applicable conditions were removed from the total number of conditions from which the compliance score was calculated during this reporting period.

4.3 DOCUMENTATION REVIEW

Initial documentation was obtained and reviewed in preparation for the assessment monitoring. Checklists were prepared based on the requirements of the EAs, EMPrs and the GA. Most relevant legal documents were available upon request during the ECO environmental monthly audit from the client and the appointed contractors, including the following:

License/Permit Holder: Red Cap Impofu (Pty) Ltd.

- The 2nd amendment of the EA for the 182MW Impofu North Wind Energy Facility (reference Number: 14/12/16/3/3/2/1102/AM2) was approved by DFFE on the 6th of December 2022. This was read together with the EA dated 25 September 2019 and the 1st amendment dated 11 November 2020.
- The 2nd amendment of the EA for the 168MW Impofu West Wind Energy Facility (reference Number: 14/12/16/3/3/2/1103/AM2) was approved by DFFE on the 6th of December 2022. This was read together with the EA dated 23 September 2019 and the 1st amendment dated 16 November 2020.
- The 2nd amendment of the EA for the 189MW Impofu East Wind Energy Facility (reference Number: 14/12/16/3/3/2/1104/AM2) was approved by DFFE on the 6th of December 2022. This was read together with the EA dated 25 September 2019 and the 1st amendment dated 16 November 2020.
- Buffer yard and concrete batching plant for the Impofu Wind Cluster (reference Number: 14/12/16/3/3/1/2776) was approved on the 24th of October 2023.
- Environmental Management Programme (EMPr) revision five and the site layout map was approved by the DFFE on the 13th of June 2023.
- Water Use Authorisation (General Authorisation – GA) for abstraction (Section 21a) of water for industrial use of two boreholes was approved on the 29th of September 2021 for the Impofu North Wind Farm.
- Water Use Authorisation (GA) for Section 21 (c, i and g) was approved on the 21st of September 2021 for the Impofu North Wind Farm.
- Water Use Authorisation (GA) for abstraction (Section 21a) of water for industrial use of two boreholes was approved on the 29th of September 2021 for the Impofu West Wind Farm.
- Water Use Authorisation (GA) for Section 21 (c, i and g) was approved on the 06th of October 2021 for the Impofu West Wind Farm.
- Water Use Authorisation (GA) for abstraction (Section 21a) of water for industrial use of two boreholes was approved on the 29th of September 2021 for the Impofu East Wind Farm.
- Water Use Authorisation (GA) for Section 21 (c, i and g) was approved on the 06th of October 2021 for the Impofu East Wind Farm.
- Water Use Authorisation (GA) for Section 22 (1) (a) (iii) was approved on the 1st of November 2019 for the abstraction of water from a registered dam for the wind farms.
- Mineral and Petroleum Resources Development Act 28 of 2002 (MPRDA) Section 53 Consent for the Impofu North Wind Farm was received on the 16th of September 2019 with no expiry date.

Monitoring documents and registers

The construction EMPr has been made part of the contract documentation with the Contractors appointed to construct the Impofu Wind Farms and associated infrastructure as required by condition 4.1.1.2 of the EMPr. Environmental training/induction is conducted by the EOs for site employees and management regarding the contents of the EA and the EMPr. Training registers are kept in the site file. Environmental Officer weekly monitoring reports are available and up to date.

Relevant environmental method statements were available and reviewed by the ECO as required by the EMPr section B section 3.1.2. Registers were available in the contractors site file such as the updated incident register; a complaint register; updated water register; an updated training register; as well as the updated waste register.

Waste Management

Domestic/General Waste

Waste separation is encouraged for recycling purposes where possible. Power Construction has appointed an independent service provider, Luvan Plant Hire (Pty) Ltd for collection and disposal of general waste at registered landfill site, Humansdorp Landfill site (permit number: 12/9/11/P53) in Kouga Local Municipality. Waste was collected from site and disposed at the landfill site on the 3rd of April 2024. Waste disposal certificates are kept in the environmental file for records. The ECO advised that the safe disposal certificates be filed for auditing and record retention purposes.

Hazardous Waste

Power Construction is planning to appoint an independent service provider to collect, transport and dispose of hazardous waste at a registered hazardous landfill facility. The hazardous waste bins are placed on a concrete slab at the site camp. The contractor was advised to avoid mixing of waste. There was no hazardous waste removed and disposed by Power during this reporting period. The ECO advised that all hazardous waste safe disposal certificates and/or waste manifests must be acquired for hazardous waste removed from site and records must be kept for audit purposes.

Sewage Waste

Power Construction (Power) appointed a service provider for chemical toilets, Bidvest Toilet Hire (Bidvest). Bidvest service, collect and dispose effluent at a registered treatment plant (Fishwater Flats Wastewater Treatment Works- licence number: 12/9/11/L433/1) at Nelson Mandela Bay Municipality. Power appointed another service provider for mobile flushable ablution facilities (Portable toilets) at the site camp. The flushable toilets are serviced by Specialized Disinfecting Services (SDS). SDS dispose their effluent at Jeffreys Bay Wastewater Treatment Works under Kouga Local Municipality (Licence number: 12/K90F/EF/4333). Bidvest serviced toilets on the 18th of April 2024 and SDS pumped septic tank on the 18th of April 2024. Chemical toiles on site are secured and anchored to the ground, to prevent them from being blown over. Waste disposal certificates available on file.

Water Consumption

Power had abstracted 1602 m^3 of water from Oyster Bay Dam from November 2023 until this reporting period. The contractor is authorised to abstract 2000 Kilolitres/ annum from the dam. Water from the dam is used for dust suppression of access roads as well as dusty working areas and to flush toilets at the site camp. At the site camp, there is a filtration system in the kitchen for consumption which is not in use yet.

Water Use Authorisations Compliance Monitoring

The water use licence (WUL) authorisations were granted in terms of GAs by the Department of Water and Sanitation (DWS) in terms of the National Water Act 36 of 1998 for the following water uses, Section 22(1) (a) (iii): a person may only use water without a licence if that water is permissible under schedule I; if that water use is permissible in terms of a general authorisation issued under section 39. The Water Use is for the abstraction of water from a registered dam that will be used during construction and for disposing sewage waste into the septic tank at the site camp. Abstraction of water from boreholes has not commenced, they are being installed. Contractor is advised to monitor water use. Registered water uses are section 21 (c, I, and g), for North there are 41 water uses, West with 50, and East with 46.



Figure 6: Water abstracted from registered Oyster Bay Dam.



Figure 7: Registered boreholes installed.

4.4 SITE ASSESSMENT

Construction activities currently underway includes clearing and grabbing, excavations for turbine foundation, stripping in road 8 and 9 at the Impofu West Farm, relocation of existing services i.e., fences and water troughs, borehole installation, erection of storage dams, and maintenance of access roads. Only activities done on Impofu East Farm includes fencing and installation of stormwater pipe for bypass road to WTG E13 and 14.

5 RESULTS OF THE AUDIT / LEGAL COMPLIANCE

EIMS have been appointed to undertake legal compliance audits in terms of the EA and generic EMPr of the Impofu Wind Farms and associated infrastructure. The results of the monthly ECO Audit are provided in this section of the report. The compliance summary, areas of good compliance, areas of concern and areas of non-compliance are provided in sections 5.1, 5.2, 5.3 and 5.4 respectively.

5.1 COMPLIANCE SUMMARY

The straight compliance score is calculated based on the compliance with the relevant conditions (i.e., yes or no). The weighted compliance score is calculated by using the compliance rating protocol (0, 2, 4) and scoring the individual conditions and calculating the percentage compliance.

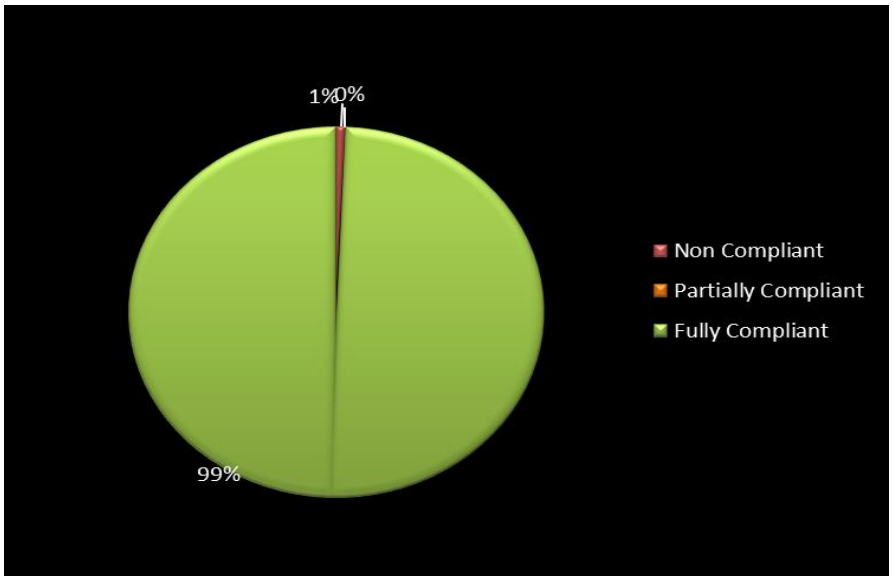


Figure 8: Summary of compliance with the requirements of the EA.

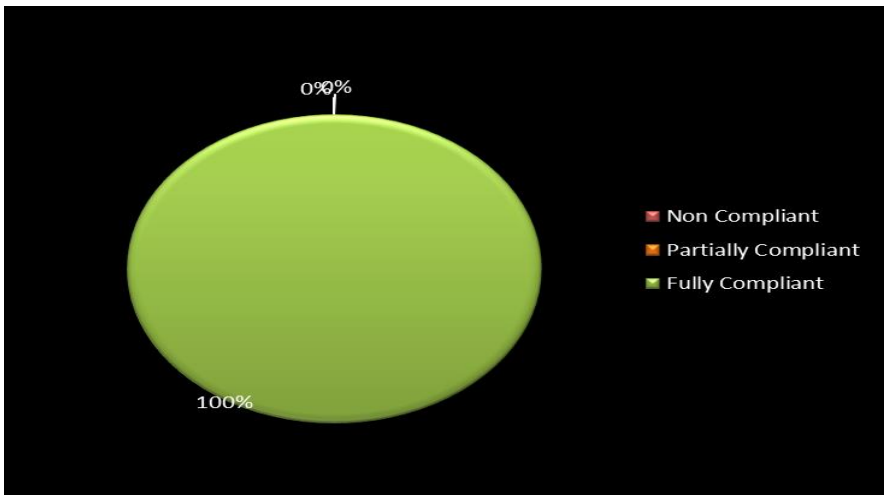


Figure 9: Summary of compliance with the requirements of the EMPr.

5.2 GOOD COMPLIANCES

Table 2: List of Good Compliances recorded during this reporting period.

Location	Category	Responsible Party	Description	Photo Reference
Site	Heritage	Power Construction	Temporary fence and 'No-Go Area' signage erected around heritage site at Impofu East.	 Figure 10: Temporary fence and appropriate signage erected around a heritage site near WTG E19, turn-around point RE25 and RE22
Site	Excavation	Power Construction	Appropriate signage erected in working areas to alert community and staff.	 Figure 11: Storage area neat and clean.

Location	Category	Responsible Party	Description	Photo Reference
Site	Stockpile	Power Construction	Stockpiles do not exceed 2 m in height on site.	 Figure 12: Stockpiles do not exceed 2 m in height.

.

5.3 AREAS OF CONCERN

Hazardous chemical storage area is not appropriate. In an instance of an accidental spillage, the bund will overflow because it is too small for the chemicals stored in it. Areas of concern have the potential to become non-compliances or incidents if not adequately considered or addressed, where required. The contractor should provide a bigger bund for its chemical storage to avoid unexpected soil contamination from an accidental spillage.

5.4 NON-COMPLIANCES

Two (2) non-compliances were noted during this reporting period. Areas of non-compliances can be escalated to Non-Compliance Report (NCR) if not adequately addressed within the timeframes agreed to.

Table 3: Environmental Non-Compliances raised during the current reporting period.

Status Description	Colour Scale
Closed Out/ Corrected	
Work in Progress (WIP)	
Open/ Uncorrected	

Non-Compliance (NC) #:	EA/EMPr Ref.	Requirement	Description of NC	Recommendation	Status	Photographic Record
001.	EA 05	Any changes to, or deviations from, the project description set out in this environmental authorisation must be approved, in writing, by the Department before such changes or deviations may be effected. In assessing whether to grant such approval or not, the Department may request such information as it deems necessary to evaluate the significance and impacts of such changes or deviations and it may be necessary for the holder of the authorisation to apply for	The project description has changed but the applicant does not have a written amendment from the Department.	The applicant should apply for project description amendment from the Department.	**Open** The applicant has not applied for amendment of the project description from the Department.	N/A



Non-Compliance (NC) #:	EA/EMPr Ref.	Requirement	Description of NC	Recommendation	Status	Photographic Record
		further environmental authorisation in terms of the regulations.				
002.	EA 06	The holder of an environmental authorisation must apply for an amendment of the environmental authorisation with the competent authority for any alienation, transfer or change of ownership rights in the property on which the activity is to take place.	It was noted that although Enel Green Power has taken over the EA and is now in the development phase of the project the EA is still states Red Cap as the Holder.	The applicant is advised to apply for amendment of the EA holder.	**Open** The applicant have to apply for amendment of the EA holder.	N/A

5.5 NON-COMPLIANCE REPORTS

Non-Compliance Reports (NCRs) are issued to the project or relevant contractor if the recorded NCs are not addressed in the agreed timeframes. Zero (0) NCRs were issued during the current reporting period.

5.6 INCIDENTS

Three (3) incidents have occurred on site and were all reported to the ECO via the EO weekly reports. On the 12th of April 2024, environmental team observed a sewage and liquid deodorizer spill at the main camp during their environmental inspection. The spill was cleaned immediately by the contractor under supervision of their EO. Calcrete was applied to the contaminated area to absorb the effluent. The absorbed material is stored in a hazardous waste bin at the site camp for safe disposal at a registered hazardous waste disposal facility. The contractor is advised to report all environmental incidents to the ECO for monitoring of requisite remedial action undertaken by the contractor following an incident.

5.7 COMPLAINTS

No new complaints were received or reported to the ECO during the reporting period. The contractor's EO mentioned that there were informal complaints that were resolved promptly. It should be noted that all complaints should be reported to the ECO as soon as they occur.

5.8 STATUS OF NON-COMPLIANCES REPORTED DURING PREVIOUS REPORTING PERIODS

This section provides the status of the non-compliances that were raised during the previous ECO Audits. There ECO recorded one (1) non-compliance during the previous audit.

Table 4: Environmental Non-Compliances raised during the previous reporting period.

Status Description	Colour Scale
Closed-Out/ Corrected	
Work in Progress (WIP)	
Open/ Uncorrected	

NC #:	EA/EMPr Ref.	Requirement	Description	Recommendation	Status	Photographic Record
001.	EA 05	Any changes to, or deviations from, the project description set out in this environmental authorisation must be approved, in writing, by the Department before such changes or deviations may be effected. In assessing whether to grant such approval or not, the Department may request such information as it deems necessary to evaluate the significance and impacts of such changes or deviations and it may be necessary for the	The project description has changed but the applicant does not have a written amendment from the Department.	The applicant should apply for project description amendment from the Department.	**Open** The applicant has not applied for amendment of the project description from the Department.	N/A



NC #:	EA/EMPr Ref.	Requirement	Description	Recommendation	Status	Photographic Record
		holder of the authorisation to apply for further environmental authorisation in terms of the regulations.				
002.	EA 06	The holder of an environmental authorisation must apply for an amendment of the environmental authorisation with the competent authority for any alienation, transfer or change of ownership rights in the property on which the activity is to take place.	It was noted that although Enel Green Power has taken over the EA and is now in the development phase of the project the EA is still states Red Cap as the Holder.	The applicant is advised to apply for amendment of the EA holder.	**Open/ uncorrected** The applicant have not applied for amendment of the EA holder.	N/A

6 CONCLUSION

The contractor is encouraged to continue to comply with all applicable environmental specifications while implementing positive environmental impact mitigation and environmental initiatives where possible.

Table 5: Summary of observations noted.

Description	Number Raised during Reporting Period	Total Number Raised	Total Number Open/ Uncorrected
Areas of Concern	**1**	**2**	**1**
Non-compliances	**2**	**2**	**2**
Non-compliance Reports	**0**	**0**	**0**
Incidents	**3**	**3**	**0**
Complaints	**0**	**0**	**0**

7 ASSUMPTIONS AND LIMITATIONS

The following assumptions and limitations apply to this report:

- The information contained in this report was sourced from information and data supplied by third parties that is assumed to be complete, valid, and true.
- This report is based on information available at the time. The information, data, observations, and evidence this report is based on is beyond the control of EIMS and may change without notice. EIMS will not be liable for any loss or damage which may arise directly or indirectly because of such changes.
- No representation or warranty, express or implied, is or will be made in relation to, and no responsibility or liability is or will be accepted by EIMS in relation to the accuracy of this report.
- Where reference is made to legislation or other statutory provisions in this report the original legislation or other statutory provisions will always take precedence and the reader is directed to revert to the original legislation or statutes.
